




# **Biscayne Bay Coastal Wetlands SFWMD Project Update**

**Leslye Waugh  
Lead Project Manager  
May 17, 2017**

# BBCW Phase I Projects

- PIR EIS Completed in July 2011-  
Revised March 2012
- 3 Project Components
  - Deering Estate
  - Cutler Wetlands
  - L31E Flow-way
- Approved by Congress in WRRDA  
2014 signed on June 10, 2014
- **PPA executed August 25, 2016**
- **Agreements for Publicly Owned  
Lands**
  - NPS September 15, 2016
  - FDEP September 22, 2016
  - MDC (Coordination ongoing  
with the County to complete the  
agreement)

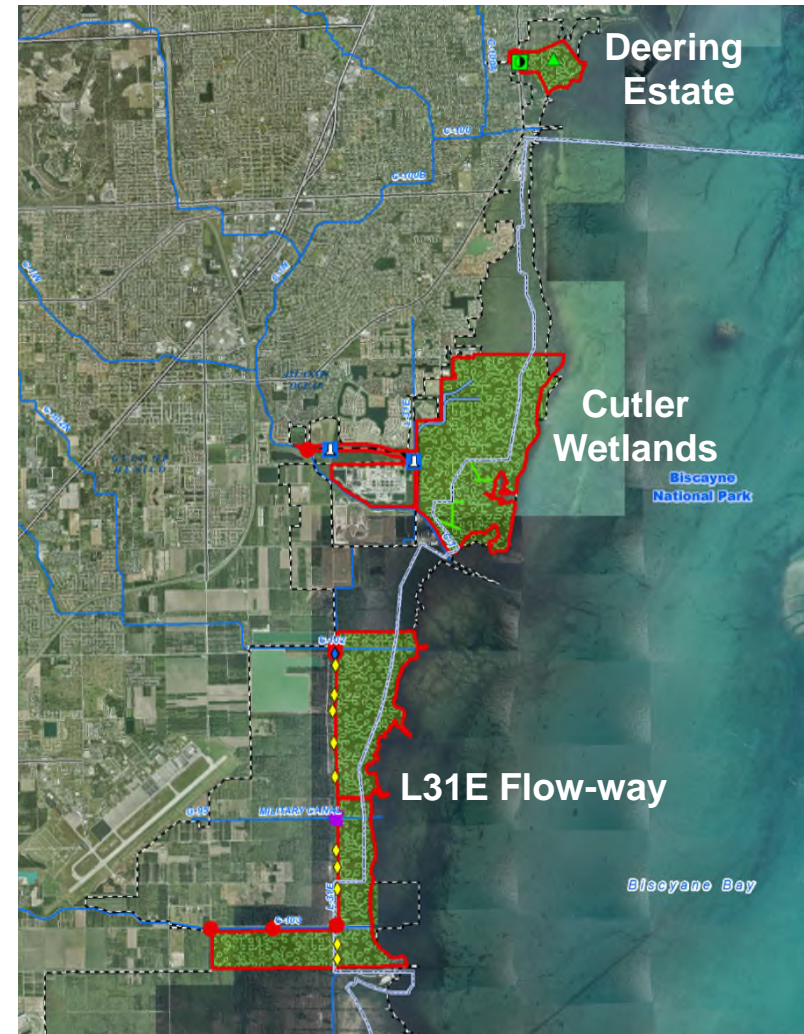



# L-31E Interim Operations




## L-31E Interim Operations

- Installation began March 2016
- Initiate operations in May 2017
- Will allow for year-round operations during various conditions
- Continue benefits observed during the pilot test
- Interim operations to continue up to 5 years or until the permanent pump station S-709 is constructed by the USACE

# SFWMD Expedited Project

## Cutler Wetlands Component

- Design completed November 2009
- Design update scheduled for 2019
- Construction scheduled 2020 to 2021


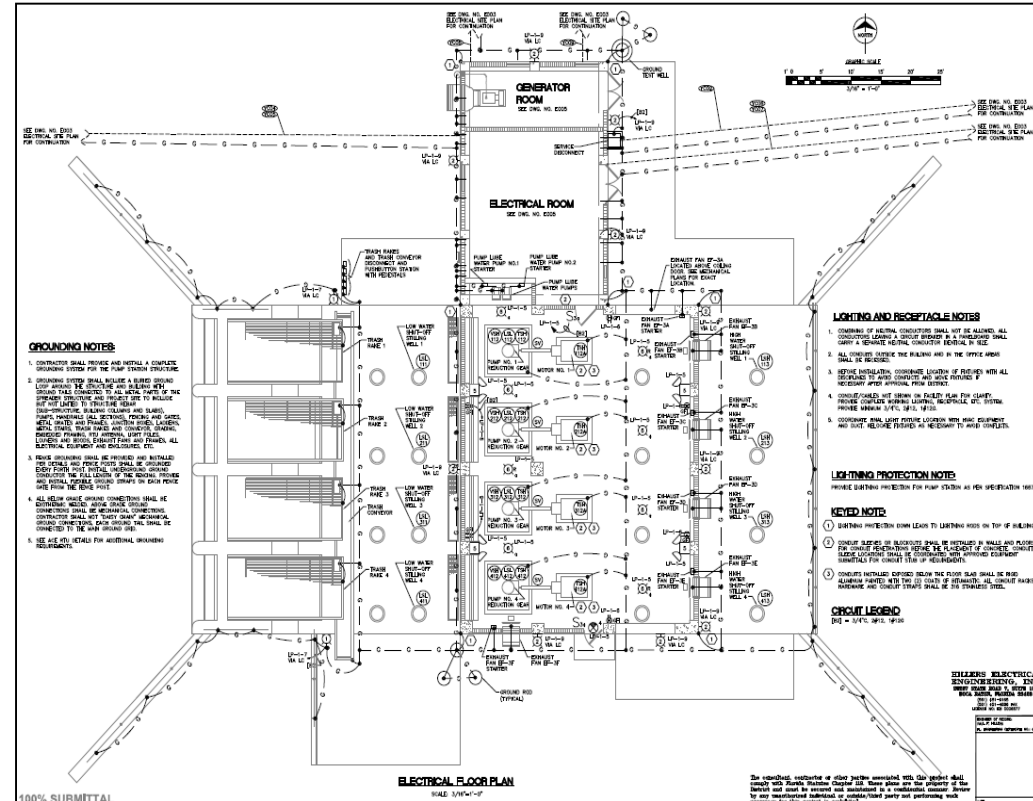




# Phase I Real Estate Acquisition


## Remaining Acres to be Acquired

Private	429 acres
FPL	193 acres
Total	622 acres

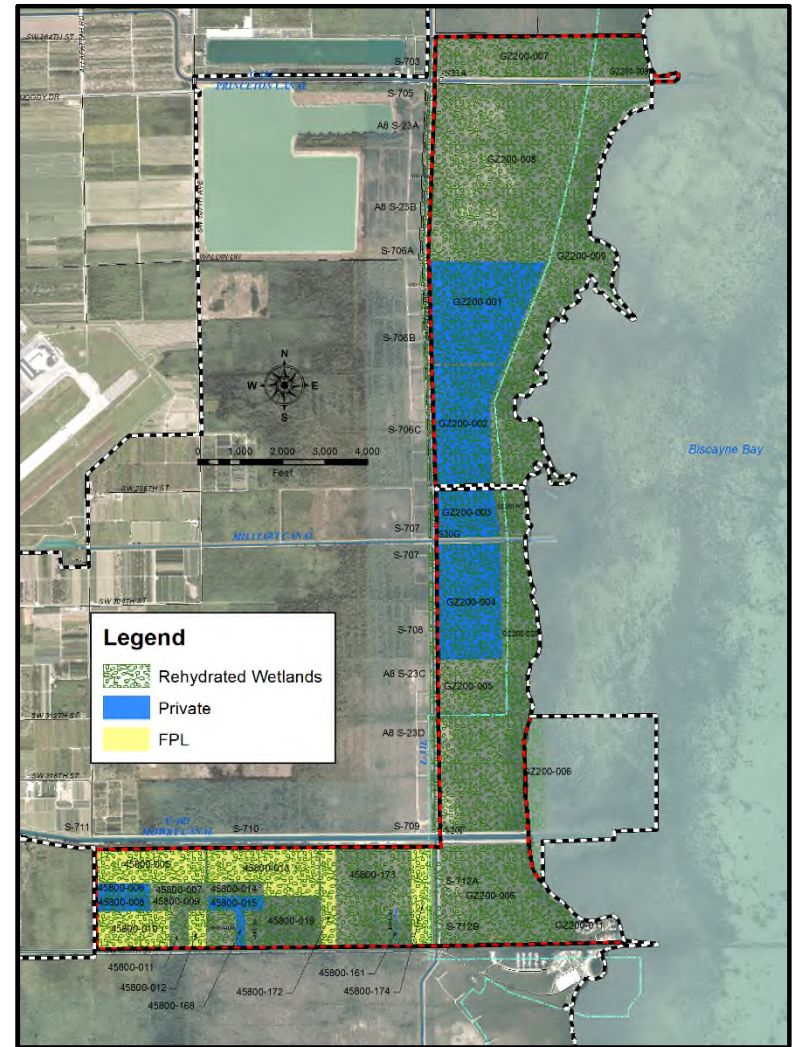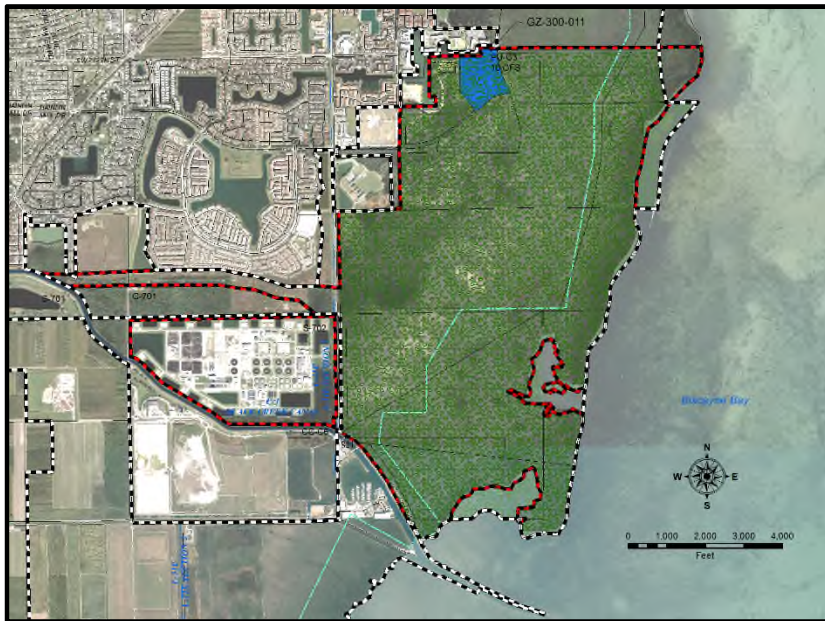



# Biscayne Bay Coastal Wetlands - Alternative O Phase II\*

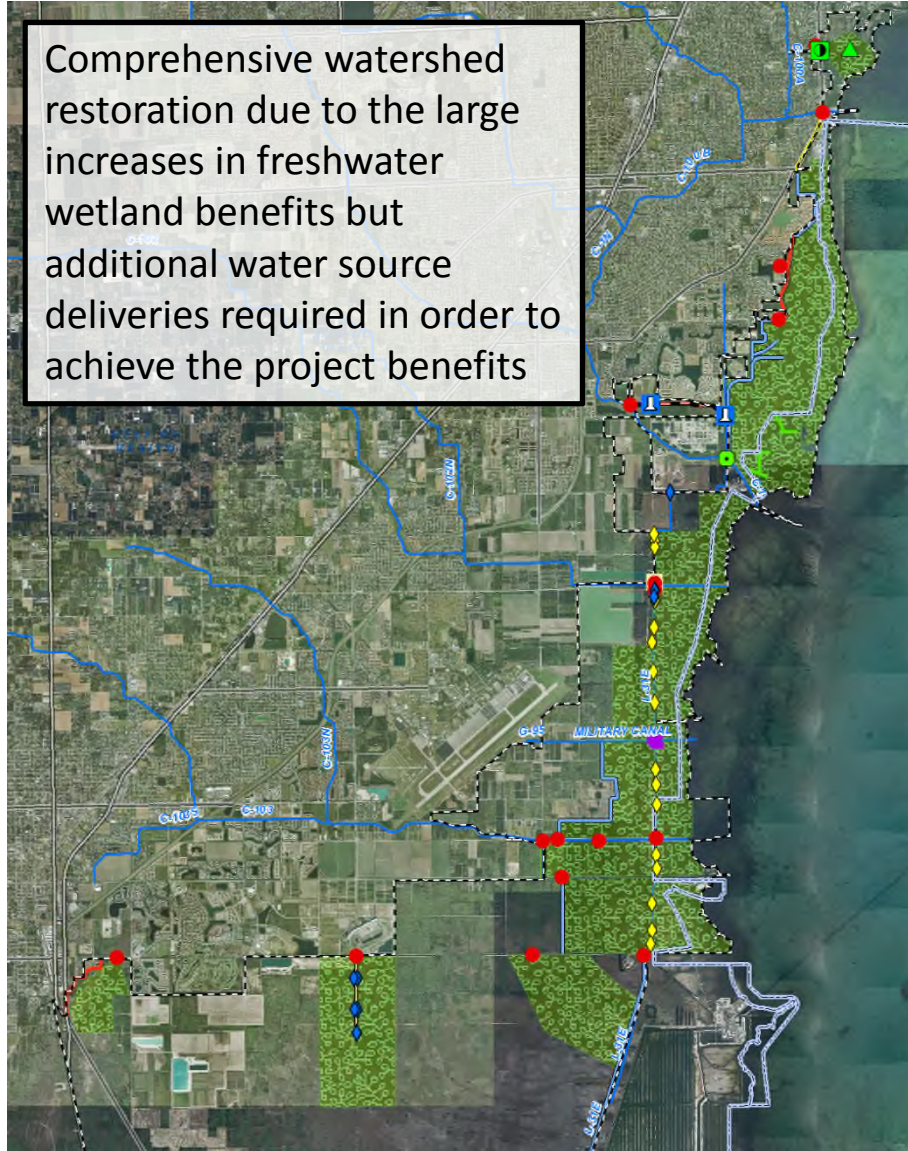

## Phase II Planning

- Integrated Delivery Schedule has BBCW Phase II planned for 2020 – 2023
- Estimated real estate acquisition approximately 4,501 acres
- Estimated PIR project cost approximately \$350 million\*

\*Does not include the cost of providing additional water source deliveries to realize the full utility of the Phase II components

# Questions?

