

SOUTH FLORIDA ECOSYSTEM RESTORATION (SFER) PROGRAM

Program & Project Update

SFER Working Group / Science Coordination Group

Howie Gonzales

05 June 2018



US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Purpose and Agenda

The purpose of this briefing is to provide participants with an overview and update on the status of the South Florida Ecosystem Restoration (SFER) program and projects.

Agenda:

- 1) Program Overview
- 2) Project Status
- 3) Key Take Aways




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Program Overview

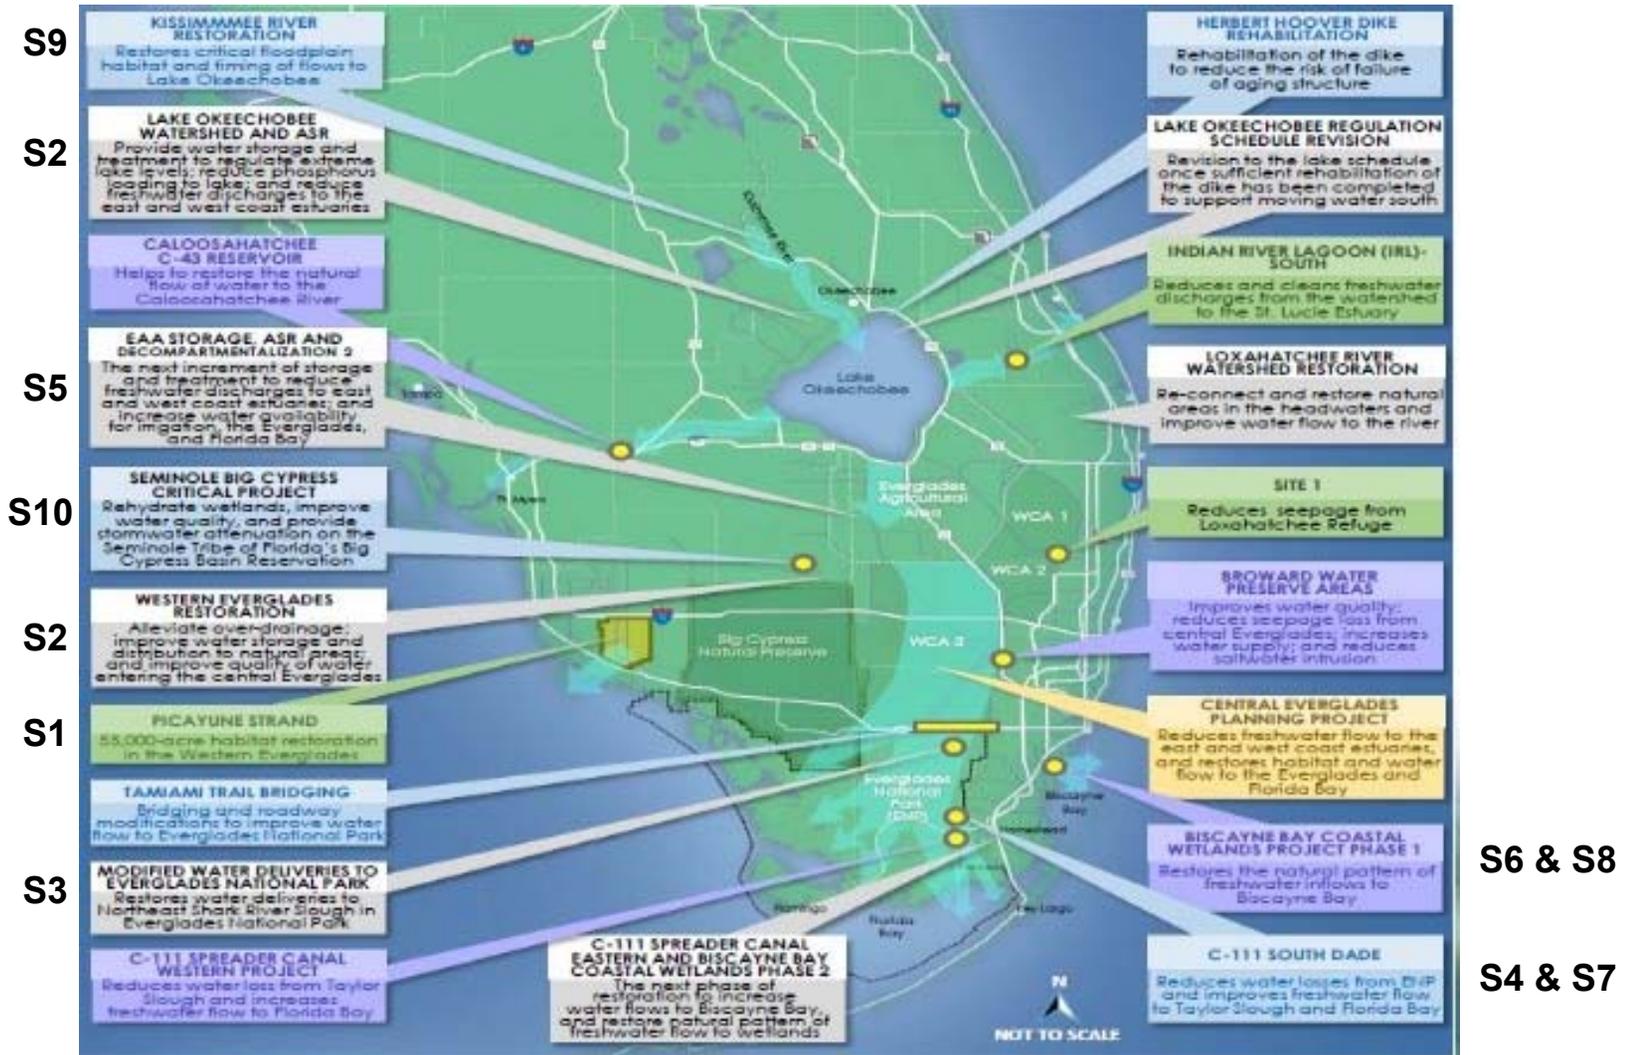

US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Recent Successes

- 1) Picayune Strand Restoration Project: Faka Union Pump Station transferred to SFWMD for OMRR&R, 09 January 2018
- 2) Lake Okeechobee Watershed Restoration and Western Everglades Restoration Projects: Project Implementation Report 3x3x3 waivers approved, 25 January 2018
- 3) Modified Water Deliveries: Tamiami Trail Bridge transferred to Florida Department of Transportation for OMRR&R, 12 February 2018
- 4) Canal 111 (C-111) South Dade: Post Authorization Change Report Agreement Executed, 16 February 2018
- 5) SFWMD (Section 203) Everglades Agricultural Area Storage Reservoir: Support Agreement executed 21 February 2018
- 6) Biscayne Bay Coastal Wetlands (BBCW): Project Partnership Agreement Amendment executed 09 March 2018
- 7) C-111 South Dade: Integral Determination Report Approved by SAD, 20 April 2018
- 8) BBCW: Contract 3 transferred to SFWMD for OMRR&R, June 2018
- 9) Kissimmee River Restoration (KRR): Director's Report Signed, 27 April 2018
- 10) Seminole Big Cypress: PCA Amendment approved by OASA(CW), 10 May 2018



US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Strong Federal Interest

- Large-scale, watershed project area (Over 18,000 square miles), including Everglades & Dry Tortugas National Park, Biscayne National Park, Big Cypress National Preserve, and other Federal Lands
- Everglades National Park is an International Biosphere Reserve, a World Heritage Site, and a Ramsar Wetland of International Importance
- Improve the health of over 2.4 million acres of south Florida ecosystem, including Lake Okeechobee
- Flood Risk Management and Water Supply for over 8 Million residents; the largest metropolitan area in the southeastern U.S. in the 3rd largest state
- 70 Federally-listed threatened and endangered species
- Robust agricultural, recreational, and tourism industries




US Army Corps
of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Partnerships and Support

- Federal Family



- South Florida Ecosystem Restoration Task Force

- 14 Members: 7 Federal, 2 Tribal, 5 State and Local Government representatives, at the Secretary/Assistant Secretary Level

- State of Florida and the South Florida Water Management District




- Tribal Nations

- Miccosukee Tribe of Indians of Florida
- Seminole Tribe of Florida



- Non-Governmental Organizations and Stakeholders

- Everglades Coalition; including Audubon of Florida and the Everglades Foundation
- Everglades Caucus, House of Representatives




US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Program Structure

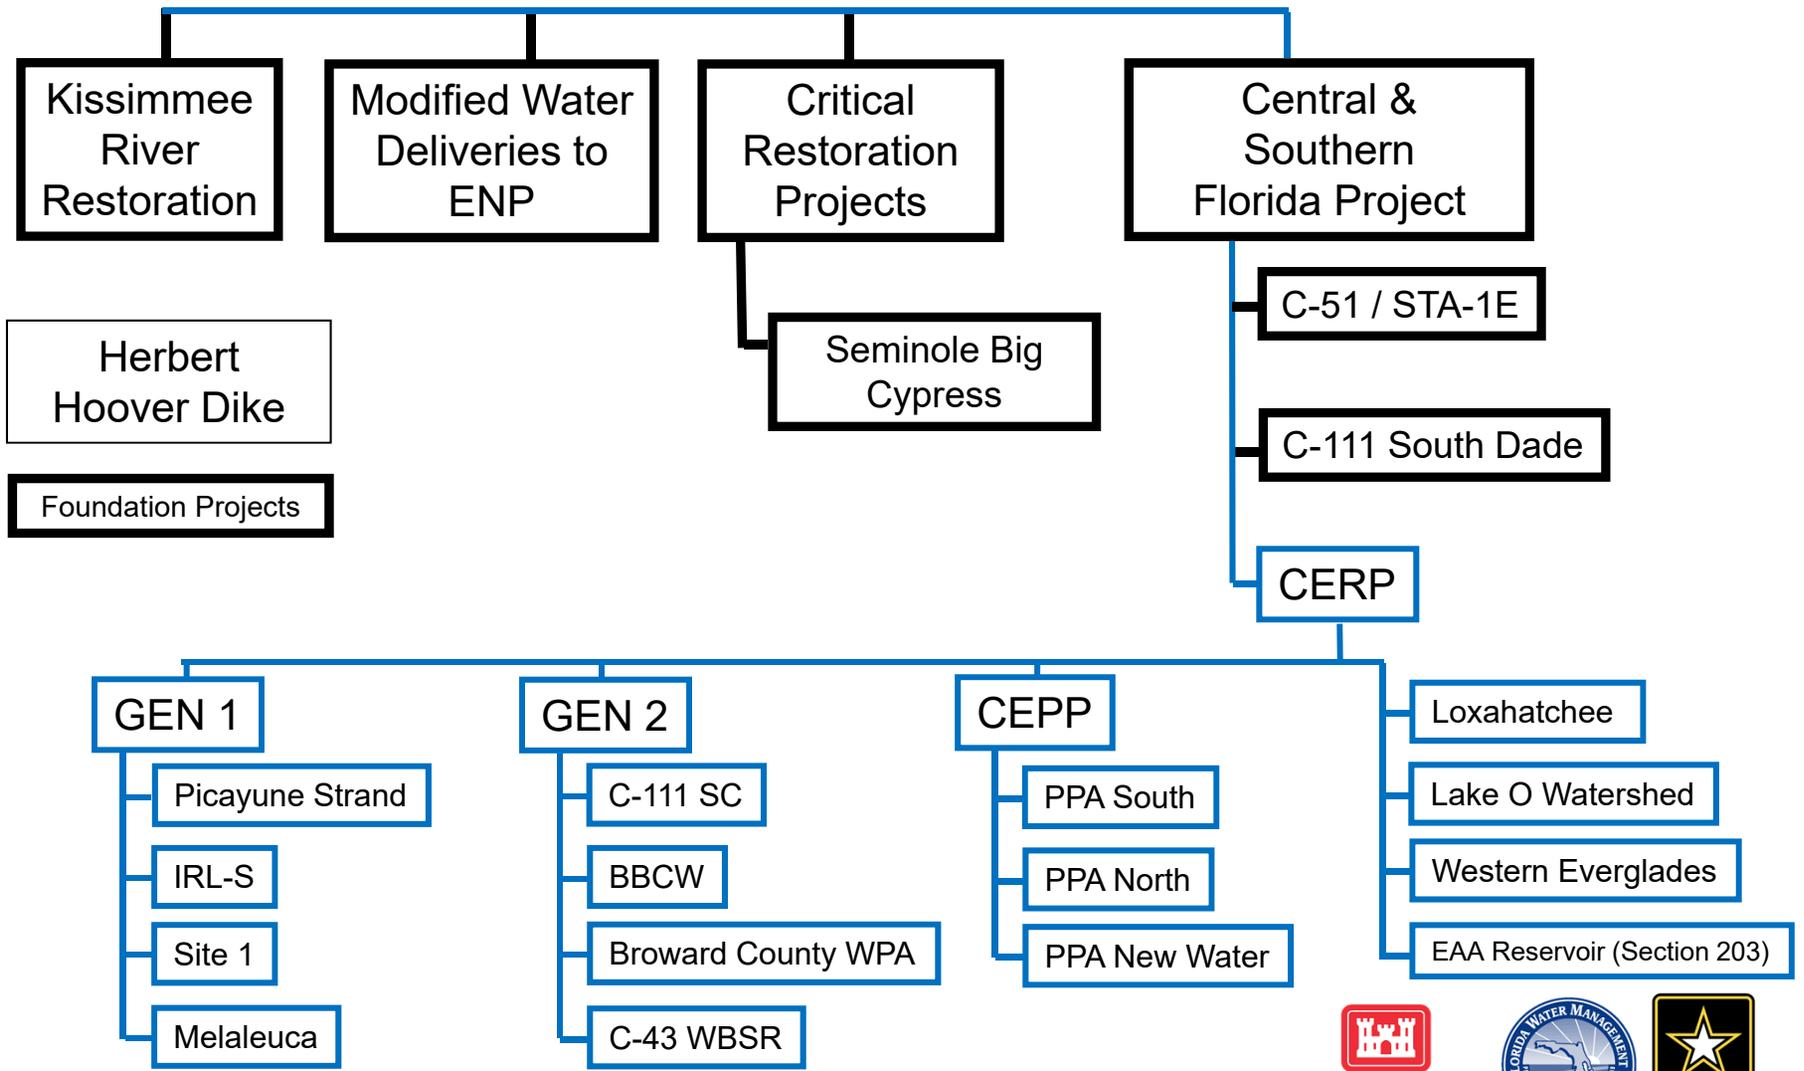


US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Kissimmee River Restoration

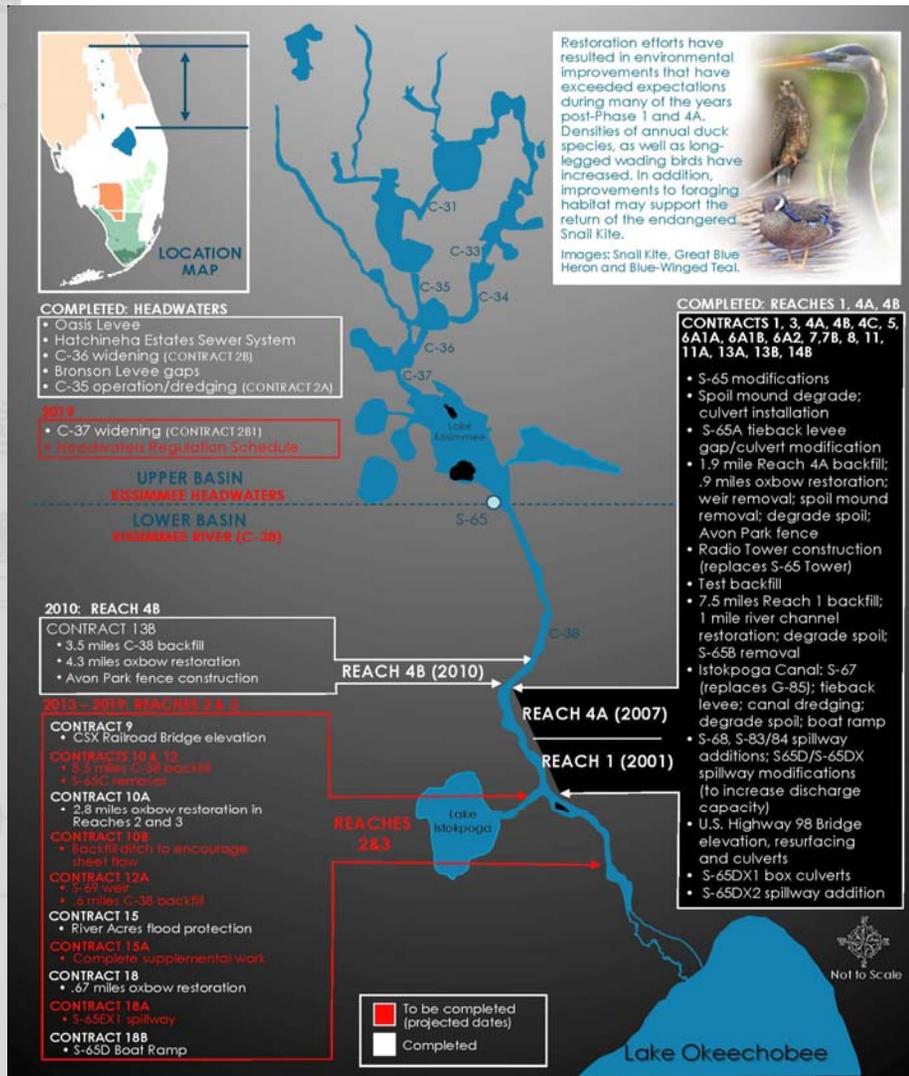

Restores critical floodplain habitat and timing of flows to Lake Okeechobee

Total Project Benefits:
Conveyance of 130,000 acre-feet of natural floodplain storage to slow the flow of water into Lake Okeechobee & reduce the impacts of high-volume discharges into the St. Lucie & Caloosahatchee estuaries.

Status:

- Completed Post Authorization Change Report (PACR) for WRDA 2018 consideration
- Final construction contracts awarded in FY17
 - C-37 Embankment Armoring
 - S-69 Weir and Canal Backfill
- Assessing and quantifying impacts from 2017 high water and Hurricane Irma
- Construction completion in 2020; initiate 5-year post construction monitoring



US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Modified Water Deliveries to Everglades National Park



Restores water deliveries to Northeast Shark River Slough in Everglades National Park

Total Project Benefits:

Storage, conveyance and seepage management improve natural water flows to Everglades National Park, provide flood mitigation for residential areas, re-connect freshwater flows, and reduce seepage losses

Status:

Construction complete in May 2018

Conducting Increment Tests. Increment 1 produced an increase in the net flow of water into Northeast Shark River Slough; extensive data has been collected to use in Increments 2 and 3




US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

C&SF: Canal 111 (C-111) South Dade

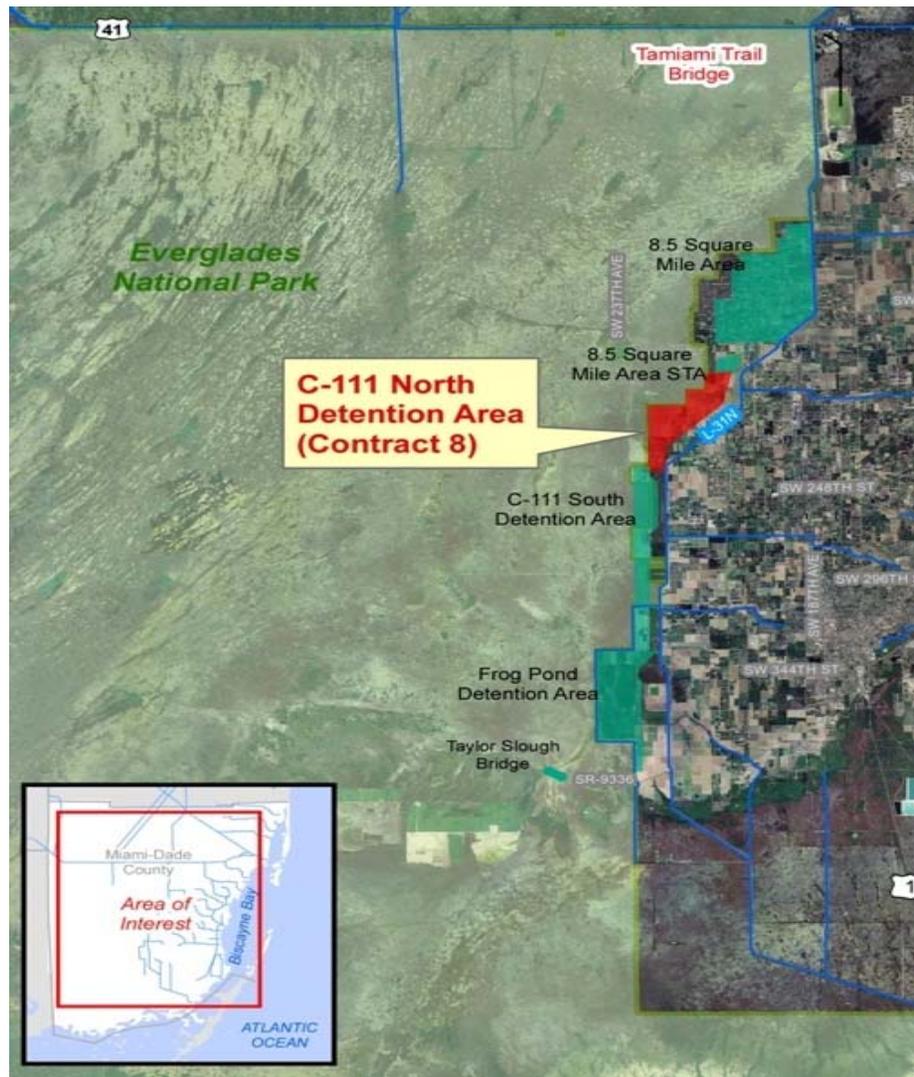

Reduces water losses from Everglades National Park and improves freshwater flow to Taylor Slough and Florida Bay

Total Project Benefits:

9,500 acre-feet of storage & seepage that reduces damaging canal discharges to Barnes Sound, reduces seepage losses from ENP, and maintains flood protection for commercial, residential, and agricultural properties to the east

Status:

Completing construction of critical project features (1 June); with balance of construction complete in fall 2018. Assessing and quantifying impacts from 2017 high water and Hurricane Irma




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Comprehensive Everglades Restoration Plan (CERP)

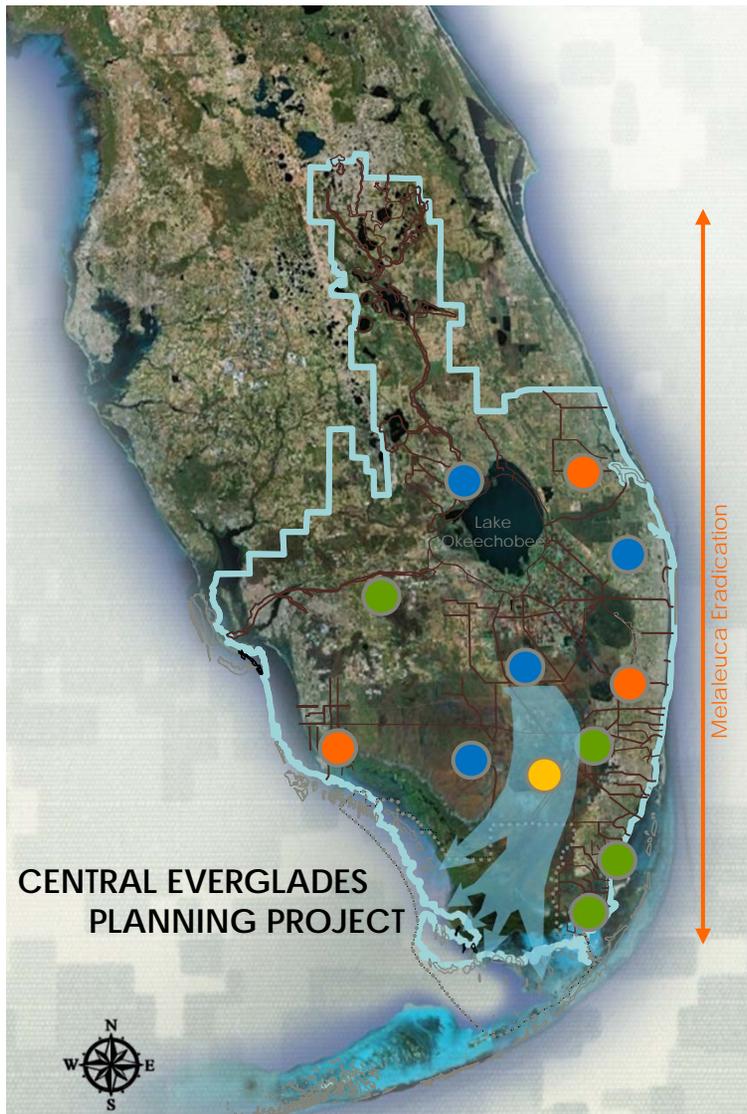

1st Generation

Site 1 Impoundment
Indian River Lagoon – South (IRL-S)
Picayune Strand Restoration Project
Melaleuca Eradication and Other Exotic Plants

2nd Generation

C-43 West Basin Storage Reservoir
C-111 Spreader Canal Western Project
Biscayne Bay Coastal Wetlands
Broward County Water Preserve Area

Central Everglades Planning Project

CERP Planning/Design

Loxahatchee River Watershed
Lake Okeechobee Watershed
Western Everglades
EAA Storage Reservoir (Section 203)




US Army Corps
of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Indian River Lagoon - South

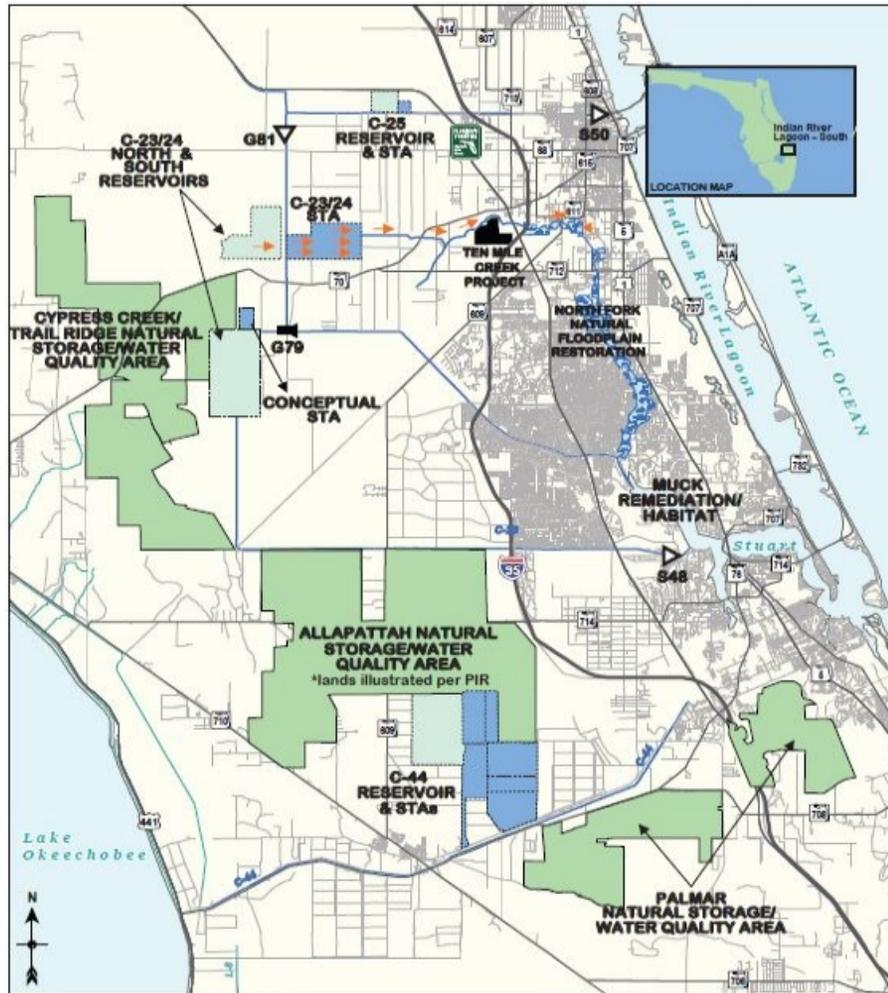

The Indian River Lagoon and St. Lucie Estuary in Martin County are two of the country's most productive and most threatened estuaries; the project will reconnect and restore natural area in the headwaters and improve water flow to the river

Total Project Benefits:

- Storage and treatment of 60,500 acre-feet local basin runoff prior to it flowing into the St. Lucie Estuary
- 12,000 acres of above ground storage
- 9,000 acres of man made wetlands
- 889 acres of restored oyster habitat
- 922 acres of submerged aquatic vegetation restored




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Indian River Lagoon – South: C-44 Reservoir / STA

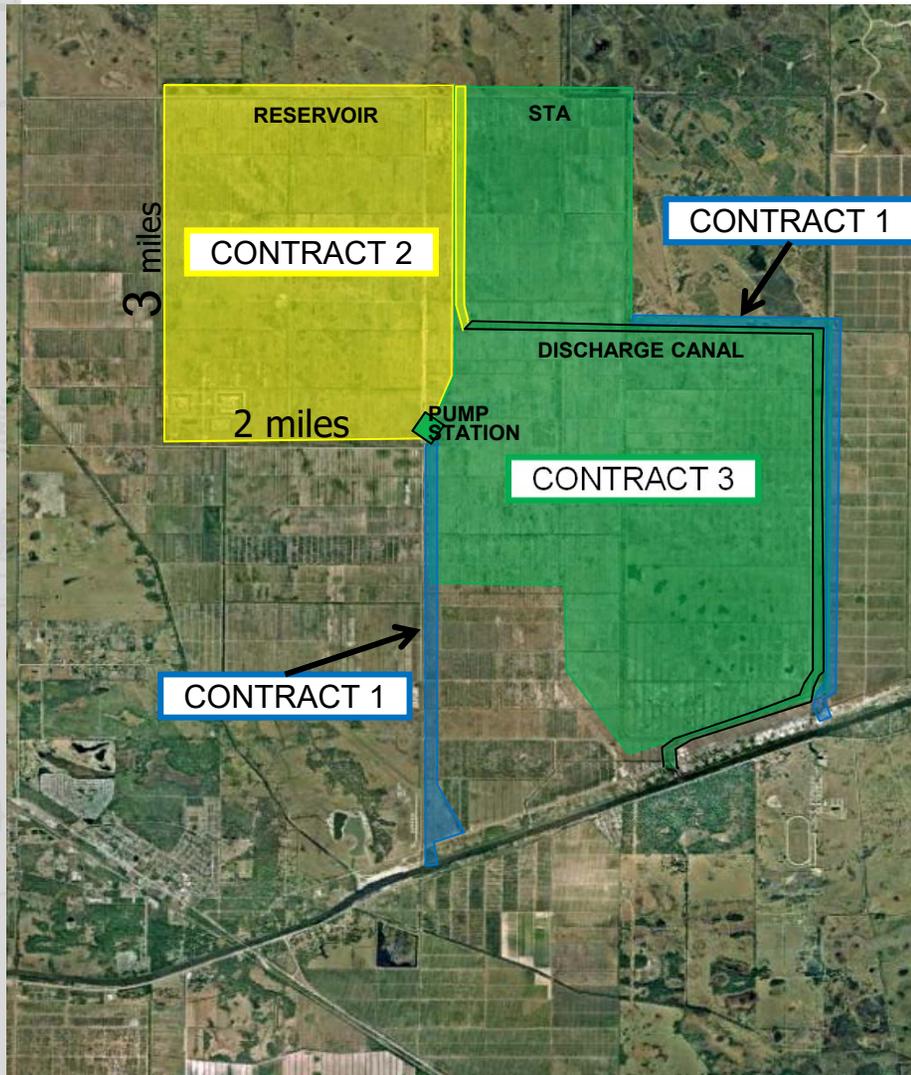

Purpose: Capture local run-off from the C-44 basin, reducing average annual total nutrient loads and improving salinity regimen for the St. Lucie Estuary and southern portion of the Indian River Lagoon.

Status:

Contract	Award	Completion
CNT-1 (USACE)	JUL 11	Completed
CNT-2 (USACE)	SEP 15	FY 2020
CNT-3 (SFWMD)		
System Discharge	SEP 14	Completed
STA	OCT 14	OCT 18
Pump Station	APR 15	DEC 18
OTMP		FY 2020-2022




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Picayune Strand Restoration Project

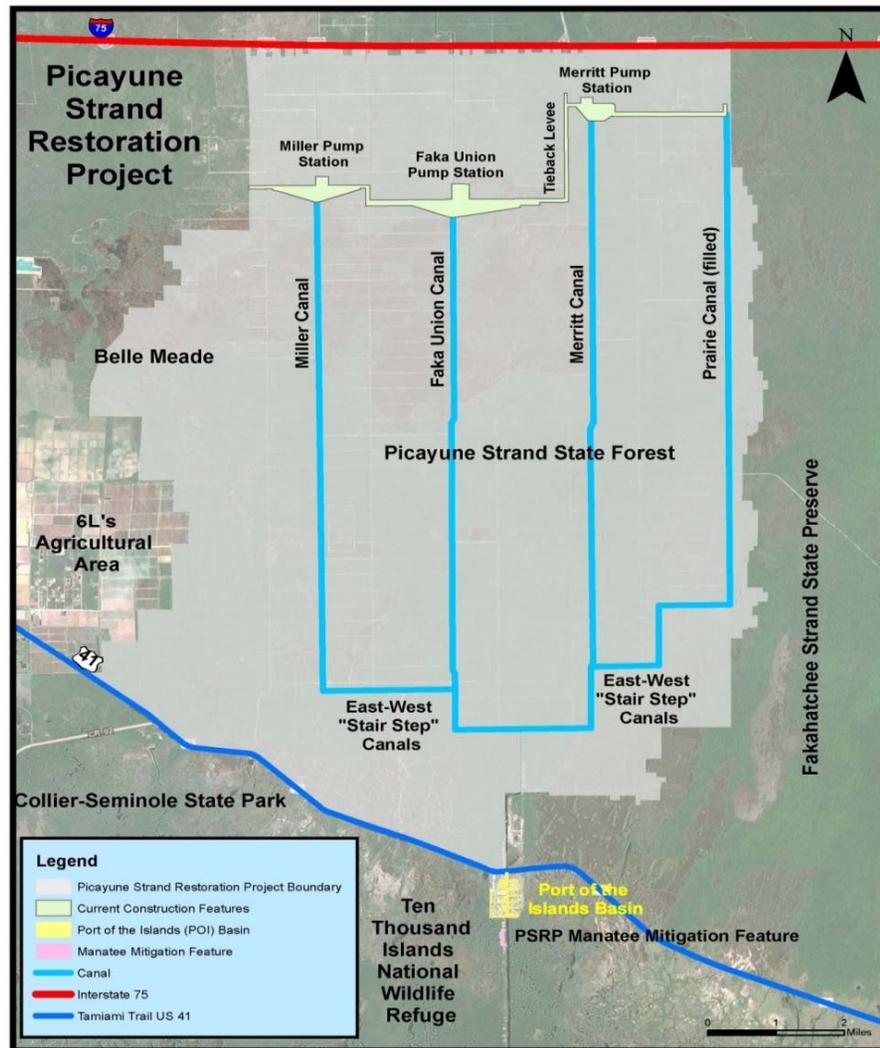

The project will restore 55,000 acres of native Florida wetlands and uplands

Total Project Benefits:

- Conveyance of water which will restore more than 55,000 acres of natural habitat
- Three pump stations: Merritt, Faka Union, and Miller
- Plugging 48 miles of canals and removing/degrading 260 miles of roads
- Features to mitigate effects of manatee refugium at the Port of the Islands Marina

Status:

- Faka Union Pump Station to O&M in January 2018
- Miller Pump Station construction completion in May 2018; initiate 1-year operational testing and monitoring period
- Design of SW Protection Features



US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Caloosahatchee River (C-43) West Basin Storage Reservoir



The project will help restore the natural flow of water to the Caloosahatchee River

Total Project Benefits:

- 170,000 acre-feet of storage that will capture & store basin stormwater runoff, along with a portion of water discharged from Lake Okeechobee, for release into the Caloosahatchee River and Estuary, as needed

Status:

- SFWMD is designing and constructing project
- Construction completion in December 2023




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Broward County Water Preserve Areas

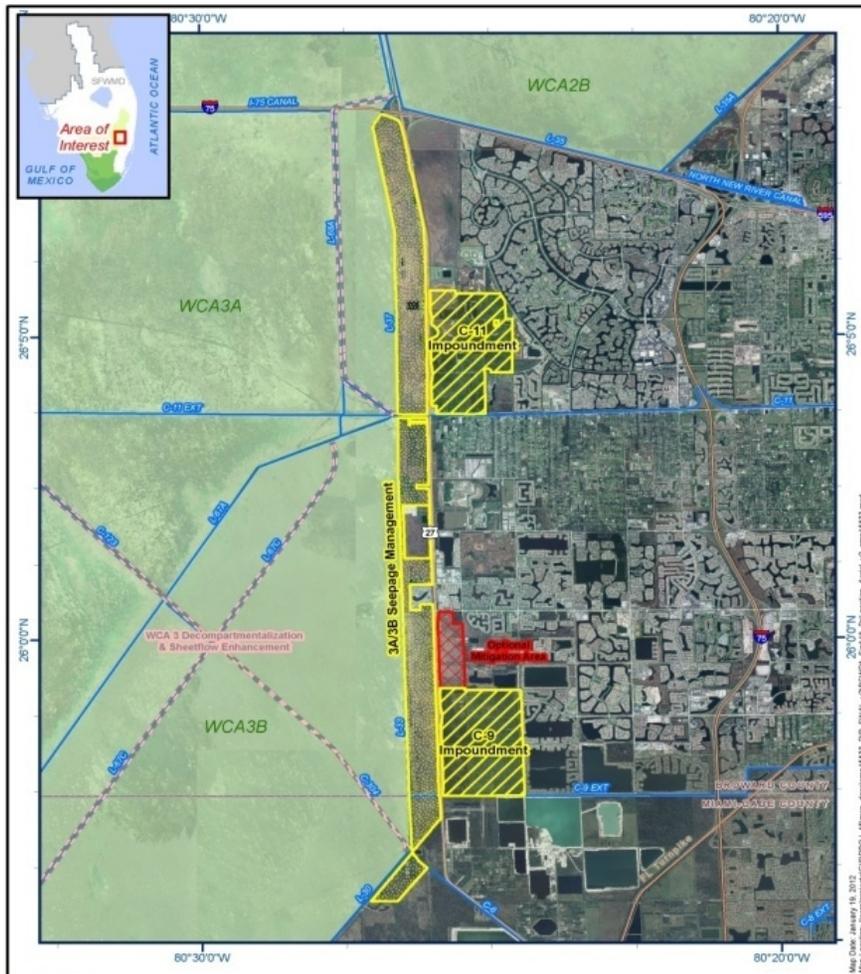

The project will improve water quality; reduce seepage loss from the central Everglades, increase water supply, and reduce saltwater intrusion

Total Project Benefits:

- 10,800 acre-feet of storage and seepage management
- Reductions in seepage losses from Water Conservation Area 3
- Capture water lost to tide for redistribution and natural system deliveries

Status:

- Initial construction contract (Mitigation Area A Berm) awarded in September 2017; construction underway
- Design of the C-11 Impoundment delayed due to funding constraints



US Army Corps
of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Biscayne Bay Coastal Wetlands


The project will restore the natural pattern of freshwater inflows to Biscayne Bay

Total Project Benefits:

- Conveyance and distribution of flows to rehydrate coastal wetlands, reduce point source discharges, and redistribute surface water; to improve the ecology of Biscayne Bay

Status:

- SFWMD completed Deering Estate and portions of the L-31 East culverts
- SFWMD constructing L-31 East components
- Design/Construction of final L-31 East components delayed due to funding constraints
- SFWMD initiates design of Cutler Wetlands in FY 2019

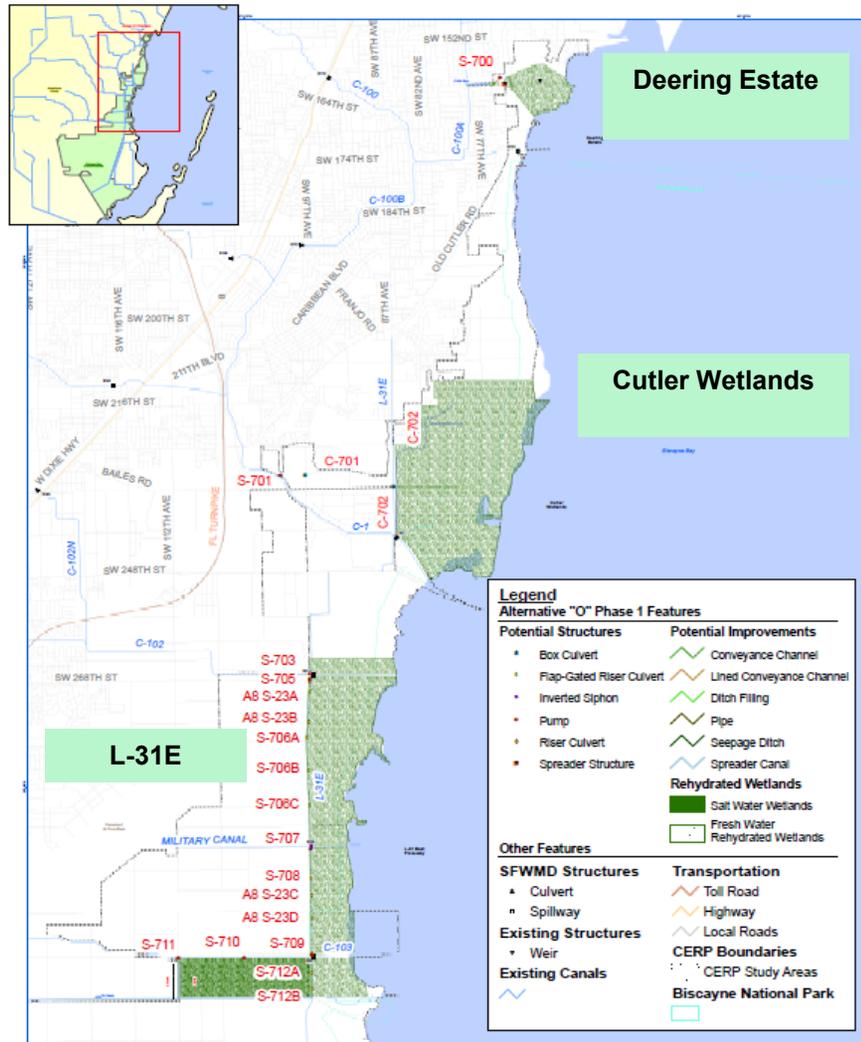


US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: C-111 Spreader Canal Western Project

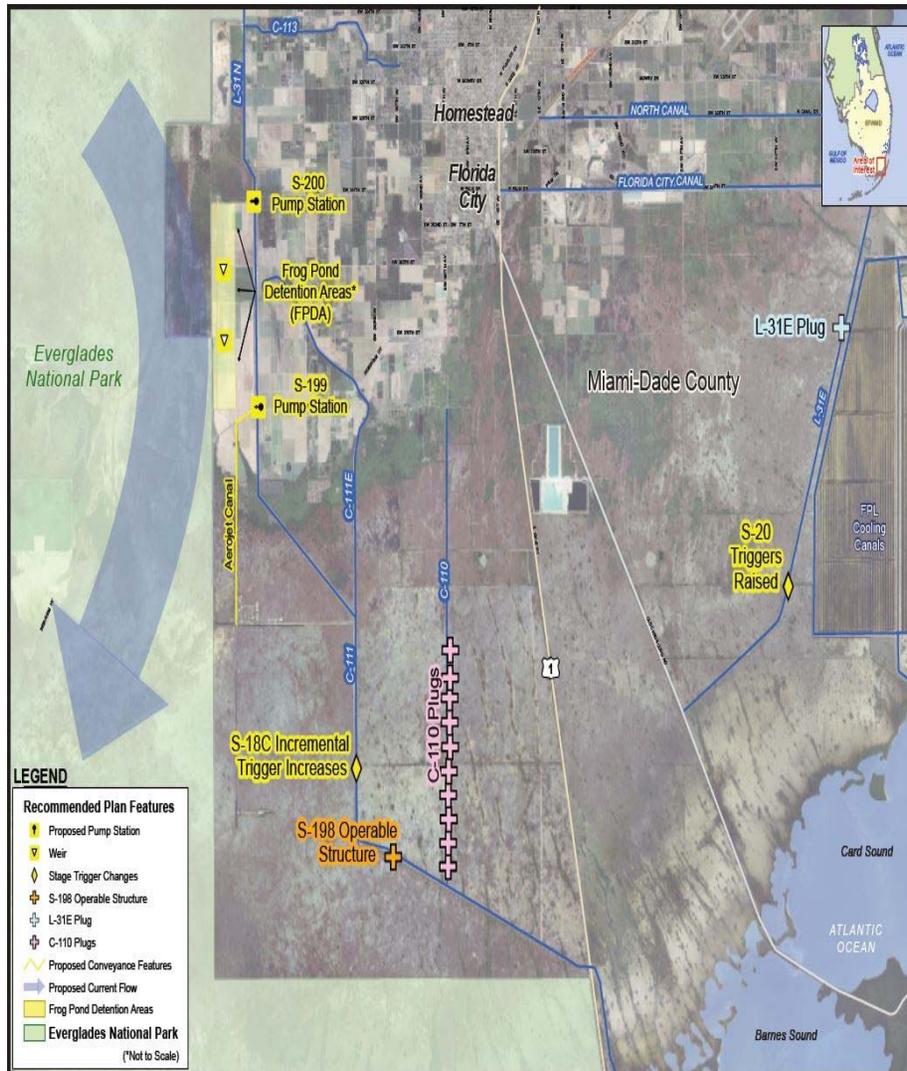

The project will reduce water loss from Taylor Slough and increase freshwater flow to Florida Bay

Total Project Benefits:

- 590 acres of conveyance and storage that will reduce seepage losses from Everglades National Park, provide increased flows to Florida Bay, and restore near-shore habitat conditions for colonies of wading birds

Status:

- SFWMD completed construction of main project features
- Project operations and monitoring indicate flow has increased by ~25% into Taylor Slough




US Army Corps
of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Central Everglades Planning Project (CEPP)

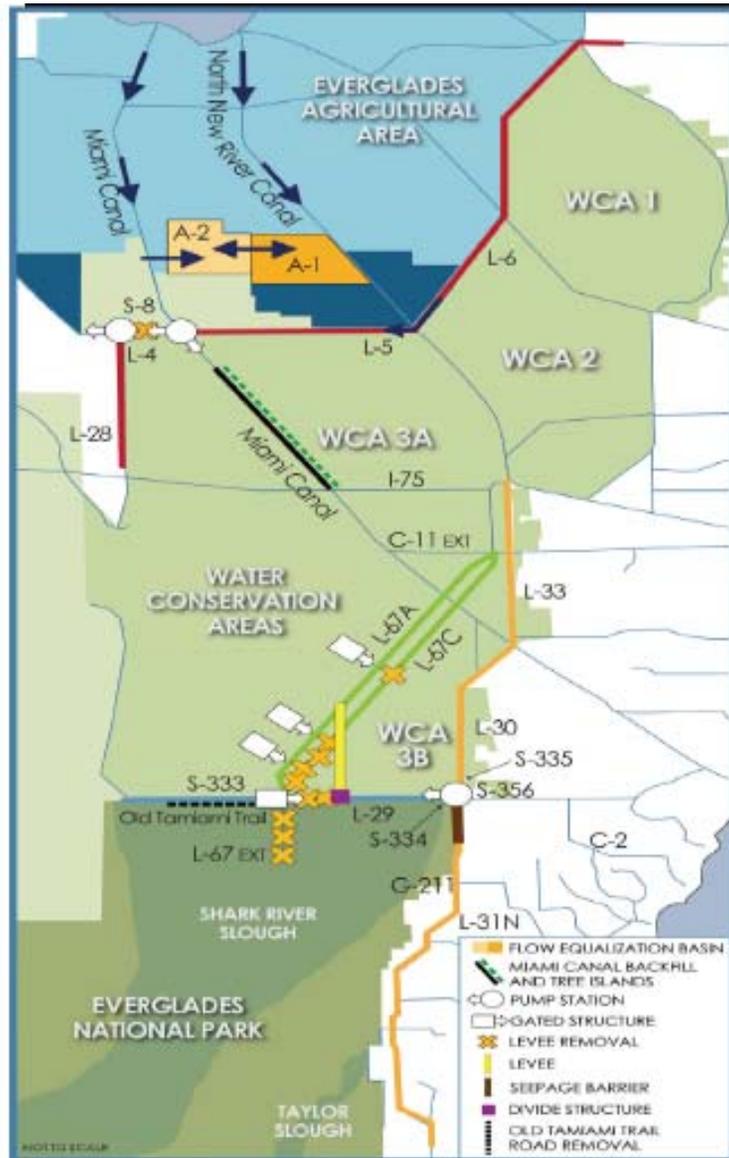

CEPP develops the next increment of project components that focus restoration on more natural flows into and through the central and southern Everglades by:

- Increasing storage, treatment and conveyance of water south of Lake Okeechobee
- Removing canals and levees within the central Everglades
- Retaining water within Everglades National Park

Status:

- CEPP South Validation initiated in October 2017
- SFWMD engaging design and construction of key CEPP South Features




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Loxahatchee River Watershed Restoration Project

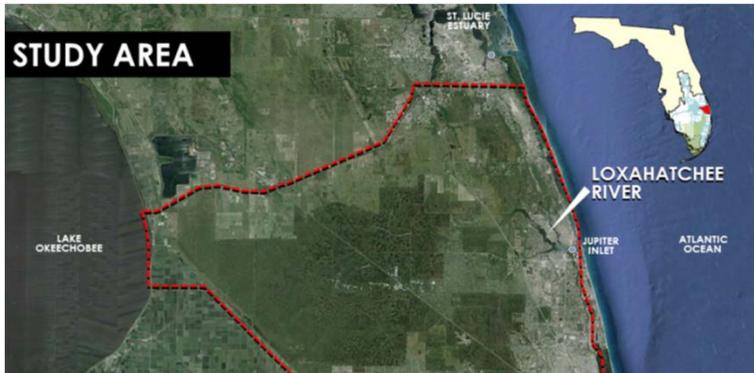

The project aims to restore and sustain the overall quantity, quality, timing, and distribution of fresh waters to the federally designated “National Wild and Scenic” Northwest Fork of the Loxahatchee River. This project also seeks to restore, sustain, and reconnect the wetlands and watersheds that form the historic headwaters for the river and its tributaries.

Status:

- SMART Planning study initiated in January 2016
- Modeling challenges have impacted study progress
- Study completion scheduled for spring 2020




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Lake Okeechobee Watershed Restoration Project

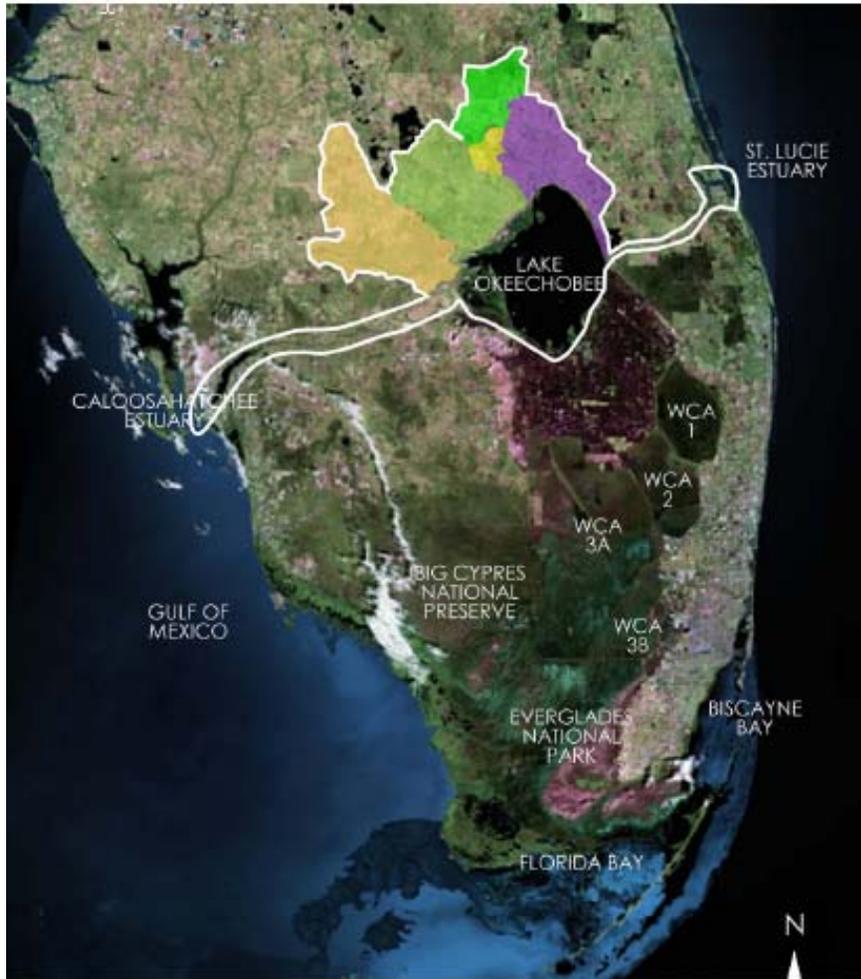

The Lake Okeechobee Watershed Project is an Everglades restoration planning effort that will improve water levels in Lake Okeechobee; improve the quantity and timing of discharges to the St. Lucie and Caloosahatchee estuaries; restore degraded habitat for fish and wildlife throughout the study area; and increase the spatial extent and functionality of wetlands.

Status:

- SMART Planning study initiated in July 2016
- Study completion scheduled for summer 2019




US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

CERP: Western Everglades Restoration Project

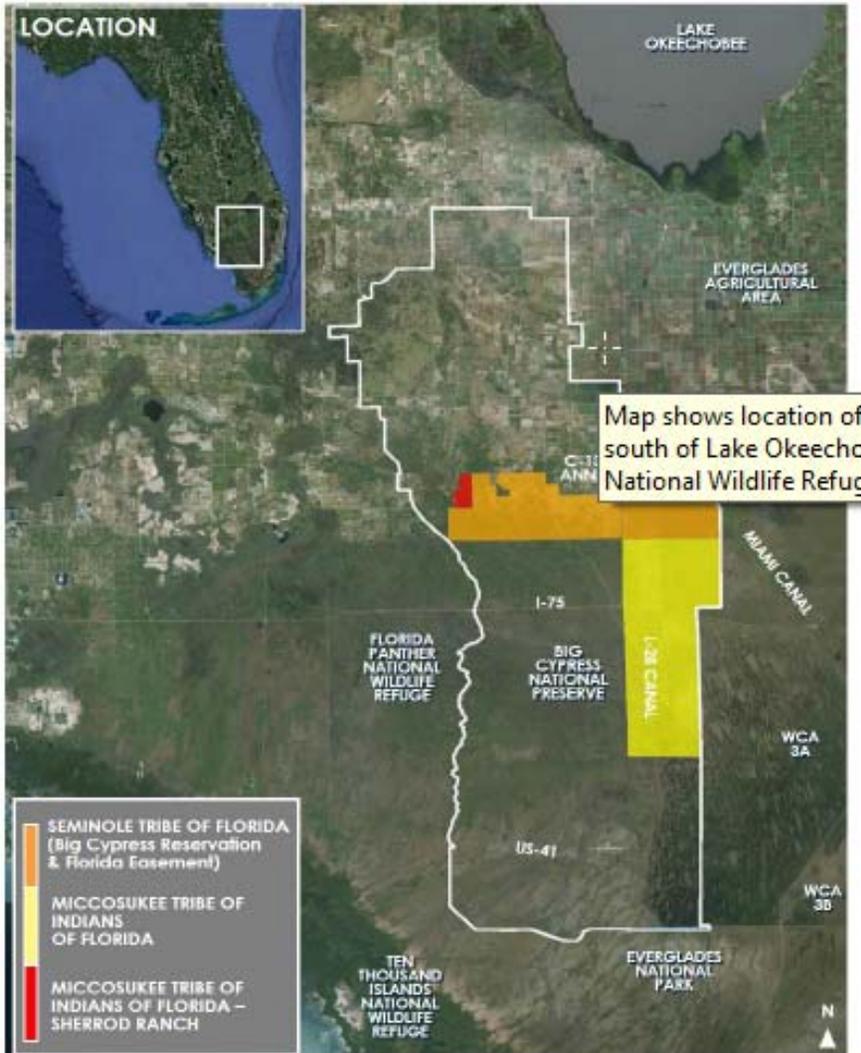

The project aims to improve the quantity, quality, timing, and distribution of water in the western Everglades and seeks to use a series of active and passive water management features and water quality features, and make alterations to existing canals and levees to reestablish sheetflow across the Big Cypress Seminole Indian Reservation and into Big Cypress National Preserve while maintaining existing levels of flood protection and water quality standards.

Status:

- SMART Planning study initiated in August 2016
- Study completion scheduled for summer 2020



US Army Corps
of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

FY18 Budget Review - Construction

SFER CONSTRUCTION	FY2018 J-Sheet	Reallocations	FY18 Adjusted Allocations	FY19 J-Sheet Budget
C&SF:WEST PALM BEACH CANAL	0	100,000	100,000	0
C&SF:SOUTH DADE COUNTY (C-111)*	0	5,240,152	6,944,152	0
Contracts 8, 8a, 9	0	3,467,000	5,171,000	0
Post Authorization Change Report	0	800,000	800,000	0
Combined Operational Plan	0	973,152	973,152	0
KISSIMMEE RIVER, FL	1,200,000	2,428,000	3,628,000	600,000
Project Oversight	1,200,000	-550,000	650,000	0
Real Estate Crediting	0	250,000	250,000	600,000
CNT's 10, 12A, Bronson Sparks	0	2,728,000	2,728,000	0
C&SF:CERP:LOXAHATCHEE	514,550	81,256	595,806	0
C&SF:CERP:LAKE O WATERSHED	0	1,371,000	1,371,000	0
C&SF:CERP:WESTERN EVERGLADES	0	2,206,000	2,206,000	0
C&SF:CERP:CEPP	400,000	600,000	1,000,000	0
C&SF:CERP:EAA	0	200,000	200,000	0
C&SF:CERP:INDIAN RIVER LAGOON - SOUTH	60,930,799	-14,378,648	46,552,151	57,945,000
Contract 2 Reservoir	60,430,799	-17,378,648	43,052,151	57,445,000
Corps Oversight of SFWMD	500,000	0	500,000	500,000
C-23/24 North Reservoir Design	0	3,000,000	3,000,000	0
C&SF:CERP:PICAYUNE STRAND	4,500,000	500,000	5,000,000	0
Faka Union, Miller Contracts	4,500,000	500,000	5,000,000	0
Design SW Protection Features	0	0	0	0
C&SF:CERP:BCWPA	0	1,360,000	1,360,000	0
NMA-A Berms EDC/SA	0	1,330,000	1,330,000	0
Design C-11 Impoundment	0	30,000	30,000	0
C&SF:CERP:BBCW	0	78,000	78,000	0
Contract 3 EDC/SA	0	48,000	48,000	0
Contract 4	0	15,000	15,000	0
Contract 5	0	15,000	15,000	0
C&SF:CERP:C-111 SPREADER CANAL WESTERN	0	10,000	10,000	0
C&SF:CERP:C-43 CALOOSAHATCHEE	1,500,000	-800,000	700,000	1,500,000
C&SF:CERP:DECOMP PHYSICAL MODEL	0	50,000	50,000	0
C&SF:CERP:PLA:PROGRAM MANAGEMENT	2,000,000	-166,000	1,834,000	2,000,000
C&SF:CERP:PLA:RECOVER	1,000,000	400,000	1,400,000	1,000,000
C&SF:CERP:AA&M	3,750,000	250,000	4,000,000	3,750,000
C&SF:CERP:PLA:INFO & DATA MGMT	200,000	200,000	400,000	200,000
C&SF:CERP:PLA:IMC	500,000	250,000	750,000	500,000
C&SF:CERP:PLA:PUBLIC OUTREACH	5,000	20,000	25,000	5,000
E&SF:PROGRAMMATIC	121,038	0	121,038	
SFER TOTAL / NET CHANGE	76,621,387	0	78,325,387	67,500,000

SFER Construction (C)

- SFER Construction budgets have declined from FY2017 to FY2019
- The Corps has used its reallocation authority to reallocate funds within the SFER Program
- The ability for the Army to ADAPT and be FLEXIBLE to changes in the SFER Program is essential to implementing the Program efficiently
- Reallocations are done to address changed conditions in project lead, changed conditions due to weather (Hurricane Irma), contract modifications, and differing site conditions



US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

FY18 Budget Review – O&M

SFER Operation and Maintenance (O&M)

- FY appropriation does not fund all SFER O&M requirements
- The Corps will not be able to satisfy the legal requirements of existing Biological Opinions in FY2019, based on the current budget in the FY2019 J-Sheet
- Federal Government has a statutory requirement to pay its share of SFER O&M
 - The Federal Government has executed Project Partnership Agreements agreeing to pay for its portion of O&M or OMRR&R
- The SFWMD budgets their OMRR&R efforts based on the legal agreements with the Federal Government
 - If the Federal Government does not pay its share of OMRR&R, the SFWMD does not have the funding needed to perform all OMRR&R

SFER OPERATION & MAINTENANCE	FY2018 J-Sheet	FY17 Work Plan for FY18 Use	FY18 Reallocations	FY18 Adjusted Allocations	FY2019 J-Sheet
C&SF:SOUTH DADE COUNTY (C-111)	0	684,000	-310,000	374,000	0
C&SF:PROGRAM MANAGEMENT	0	1,110,000		1,110,000	0
C&SF:MANATEE PASS GATES	0	224,000		224,000	0
C&SF:CERP:INDIAN RIVER LAGOON - SOUTH	0	0		0	0
C&SF:CERP:PICAYUNE STRAND	0	0		0	0
C&SF:CERP:C-111 SREADER CANAL	0	0		0	0
C&SF:CERP:BBCW	0	0		0	0
C&SF:CERP:SITE 1	0	113,000		113,000	0
C&SF:CERP:MELALEUCA ERADICATION	0	0		0	0
E&SF:SEMINOLE BIG CYPRESS	0	63,000		63,000	0
MODIFIED WATER DELIVERIES TO ENP	0	638,000	310,000	948,000	0
SFER TOTAL / NET CHANGE	0	2,832,000	0	2,832,000	0



US Army Corps of Engineers



SOUTH FLORIDA ECOSYSTEM RESTORATION PROGRAM

Key Take Aways

Strong Federal Interest

Strategic Partnerships

Continued progress in all phases: planning, design, construction, operations & maintenance

Continued Administration and Congressional Funding

www.evergladesrestoration.gov



US Army Corps
of Engineers.



SOUTH FLORIDA ECOSYSTEM RESTORATION (SFER) PROGRAM

Program & Project Update

SFER Working Group / Science Coordination Group

Howie Gonzales

05 June 2018



US Army Corps
of Engineers

