

# SOUTH FLORIDA ECOSYSTEM RESTORATION (SFER) PROGRAM

Integrated Delivery Schedule (IDS)  
2019 Update - Working Version  
Public Workshop Hosted by SFER Task Force

Eva B. Vélez  
19 September 2019



®



## OVERVIEW -- IDS 2019 UPDATE

- IDS Purpose and Background
- Review of July 2018 IDS (see handout)
- Highlights of FY2019 Activities
- IDS 2019 Update – Working Version (see handouts)



US Army Corps  
of Engineers.



## PURPOSE OF TODAY'S WORKSHOP

Educate the public on the process to update to the Integrated Delivery Schedule for the SFER

Increase transparency with stakeholders and the public on how projects fit together

Receive comments on the Working Version of the 2019 IDS update



US Army Corps  
of Engineers.





Pre-development  
"River of Grass"



Extensive Agricultural  
Development of  
Muck Lands

mid 1800s



Settlement Continues

early 1900s



1926 & 1928

Catastrophic  
Hurricanes


WRDA 2000

CERP  
Authorized



C&SF Authorized

1948

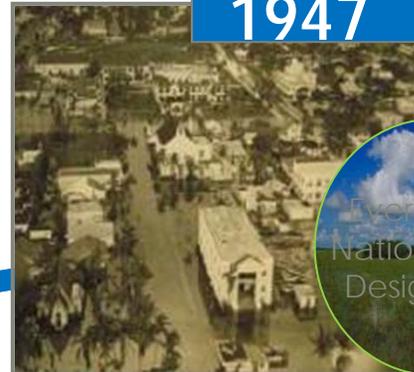

Extensive Floods

1947



Muck Fires

1930s

# HOW & WHY


SOUTH FLORIDA EVERGLADES RESTORATION PROGRAM



US Army Corps  
of Engineers.



# COMPREHENSIVE EVERGLADES RESTORATION PLAN (CERP)

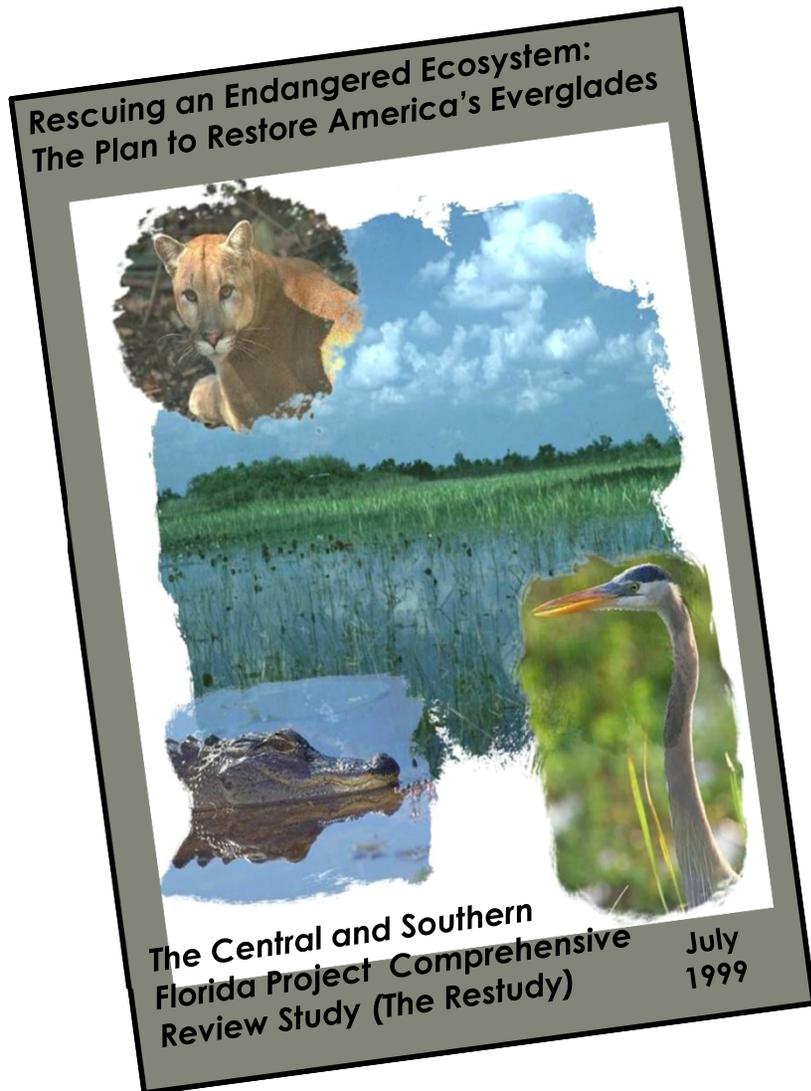

On December 11, 2000, the President signed the Water Resources Development Act of 2000 approving:




A program providing for the restoration, preservation, and protection of the south Florida ecosystem while providing for other water-related needs of the region.




US Army Corps  
of Engineers.



# THE GOAL OF CERP

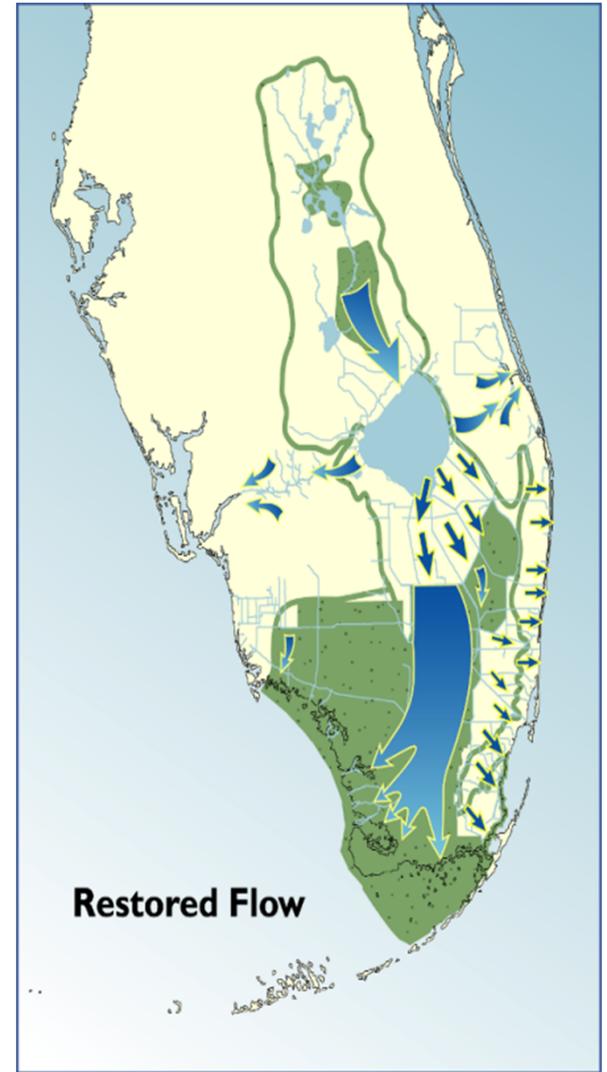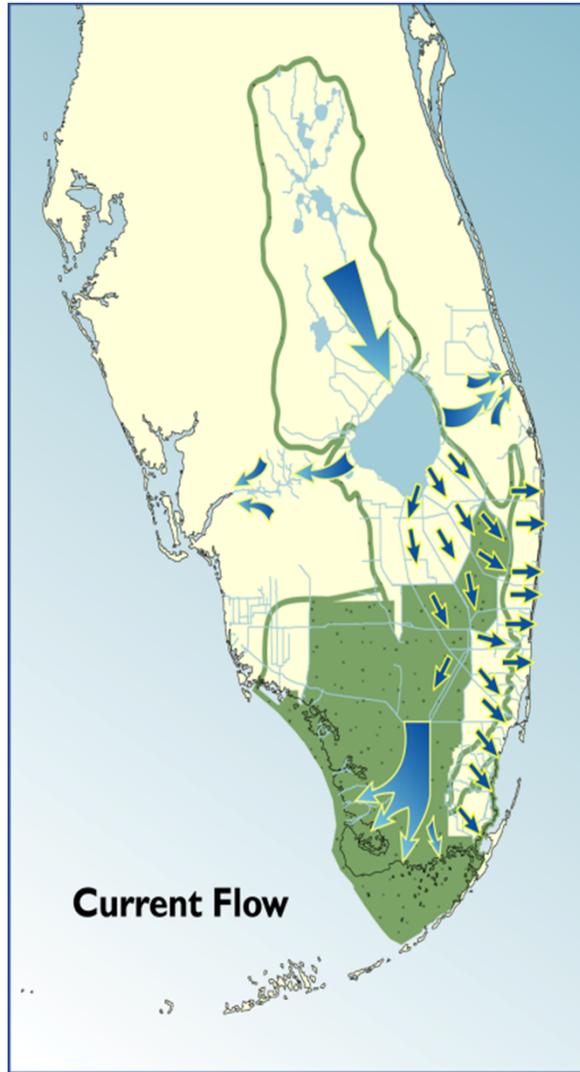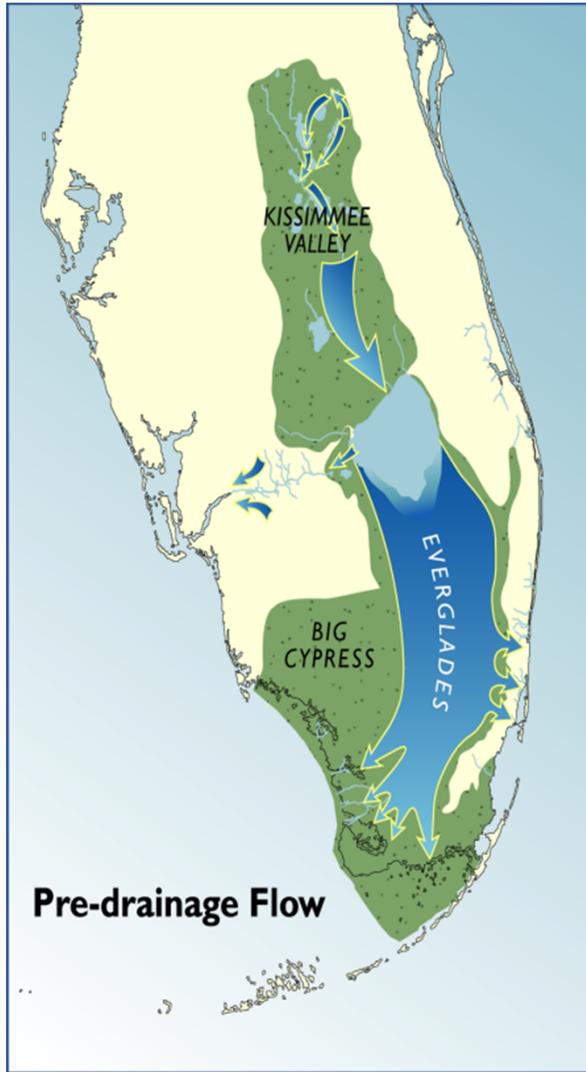

Q/Q  
T/D



US Army Corps  
of Engineers.



# HISTORY OF THE INTEGRATED DELIVERY SCHEDULE

## Yellow Book (1999)

- Contained implementation plan with GANTT chart showing sequencing of CERP projects
- 35+ Year implementation period
- Coordinated with stakeholders prior to inclusion in Yellow Book
- Based on annual funding level of \$200M Federal and \$200M non-Federal

## Master Implementation Sequencing Plan (MISP)

- Required by Programmatic Regulations
- To maximize the achievement of the goals and purposes of the plan at earliest possible time and in the most cost-effective way
- Completed in 2005, projects sequenced within 5-year bands
- Integrated foundation projects and other projects CERP depends upon to create an “**Integrated Delivery Schedule**” in 2008



US Army Corps  
of Engineers.

